



Bandlaufschemata Grube

Übersicht Bandanlagen - Jahre 2020 - 2023

3x SRs 1300-1504/ -1506/ -1523
+ 3x BRs 1400-707/ -730/ -738

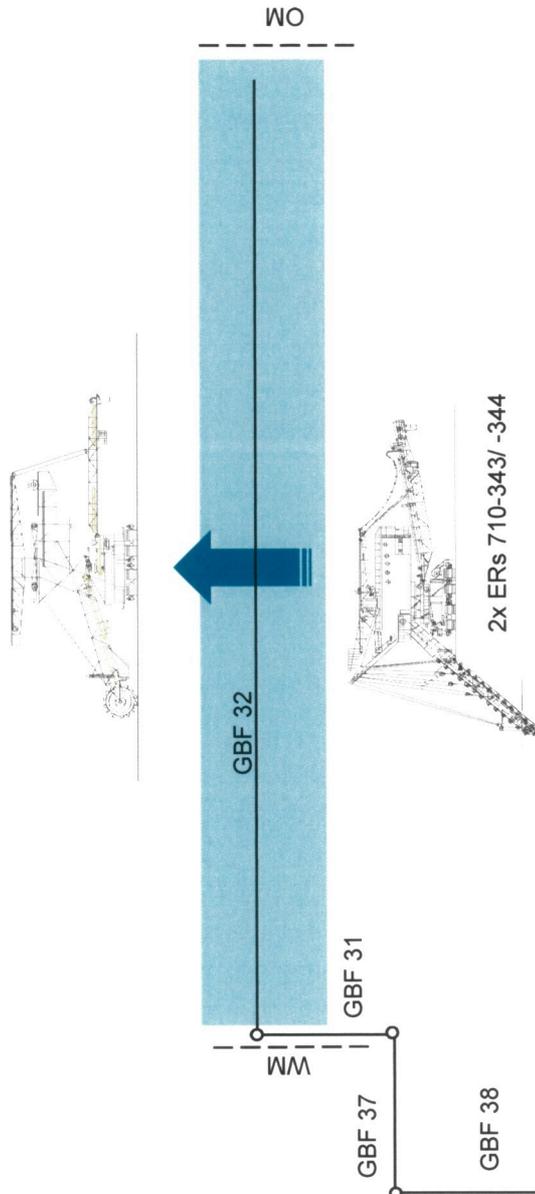

GBF	P (kW)	B (mm)	V (m/s)	Gurtqualität	L (m)		L (m)		L (m)	
					Anfang 2020	Ende 2020	Ende 2021	Ende 2022	Ende 2023	
32	4 x 900	2.000	6,03	St 2500	2.730	2.920	2.985	2.920	2.920	2.920
31	3 x 900	2.000	5,9	St 2500	2.555	2.835	2.995	3.315	3.490	3.490
	4 x 900									
37	2 x 900	2.000	4,9	St 2500	1.078	1.078	1.078	1.078	1.078	1.078
38	3 x 1.250	2.000	4,9	St 2500	3.465	3.465	3.465	3.465	3.465	3.465
39	4 x 900	2.000	5,6	St 2500	1.940	1.940	1.940	1.940	1.940	1.940
40	2 x 900	2.000	4,9	St 2500	495	495	495	495	495	495
					12.263	12.733	12.958	13.213	13.388	13.388

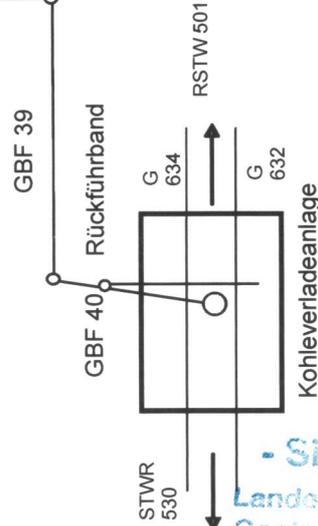

Sichtvermerk
Landesamt für Bergbau,
Geologie und Rohstoffe
Brandenburg
